

BES(T)POKE
Software Development Plan

Berk Mertoğlu
Atakan Coşar
Zeynep Durmuş
Aslı ARAS
Ata Barış Kuğu
Berkay KOÇ
Eralp Çolakoğlu
Arzum Naz Güney

17.05.2026

Contents

Contents.....	1
1.0 Overview.....	3
1.1 Problem Definition.....	3
1.2 Background Information.....	3
1.3 Objectives.....	4
2.0 High-Level Functionality.....	5
2.1 Functional Requirements.....	5
2.2 Non-Functional Requirements.....	8
3.0 Software Tools.....	9
3.1 Deployment Platform — AWS.....	10
3.2 Frontend Framework — React.js.....	10
3.3 Backend Framework — .NET Core (ASP.NET Core).....	11
3.4 Database — MS SQL Server.....	12
3.5 Payment / Escrow — Iyzico.....	13
4.0 Software Process Model.....	14
5.0 Schedule and Effort.....	17
6.0 Stakeholders and Project Risks.....	20
6.1 Stakeholders.....	20
Table 6.1 — Stakeholders.....	20
Table 6.2 — Risk Analysis Matrix.....	22
7.0 Measurements.....	25
Table 7.1 — Measurements.....	25
8.0 Graphical User Interfaces.....	27
8.1 Customer's Interfaces.....	27
8.1.1 Homepage.....	27
8.1.2 Customer Registration Page.....	28
8.1.3 Customer Sign-In Page.....	29
8.1.4 Customer Home Page.....	29
8.1.5 Customer Home Page With Dropdown Menu.....	30
8.1.6 Music Services Page.....	31
8.1.7 Creator Profile Page (Customer View).....	32
8.1.8 Creator's Previous Works.....	33
8.1.9 Creator's From Example.....	34
8.1.10 Customer Chat Box.....	35
8.1.11 Escrow Payment Page via Iyzico.....	36
8.1.12 Customer Order Page.....	38
8.1.13 Customer Profile.....	39
8.1.14 Account Settings Page.....	40
8.1.15 Help and Support Page.....	40
8.1.16 Active Order Tracking.....	41
8.2 Creator's Interfaces.....	42
8.2.1 Creator Registration Page.....	42

8.2.2 Creator Sign-In Page.....	42
8.2.3 Creator Home Page.....	43
8.2.4 Creator Home Page With Dropdown Menu.....	44
8.2.5 Creator Profile.....	45
8.2.6 Creator Form Editor Page.....	46
8.2.7 Creator Previous Works Page.....	47
8.2.8 Creator Edit Profile Page.....	48
8.2.9 Account Settings Page.....	49
8.2.10 Help and Support Page.....	49
8.2.11 Creator Chat Box Page.....	50
8.2.12 Creator Current Works.....	51
8.3 Admin's Interfaces.....	52
8.3.1 Admin Log in Page.....	52
8.3.2 Admin Dashboard.....	53
8.3.3 Dispute Management.....	54
8.3.4 User Management.....	55
8.3.5 Content Moderation.....	56
8.3.6 System Settings.....	57
9.0 Conclusion.....	58

1.0 Overview

The Bes(t)poke project is developed to address communication, payment security, and workflow management problems commonly experienced in freelance commission platforms. Existing commission processes are usually handled through fragmented social media communication and external payment systems, which often create misunderstandings, payment disputes, and inefficient revision cycles. To solve these issues, Bes(t)poke introduces a centralized marketplace platform that combines structured commission forms, integrated messaging, escrow-based payment handling, and project tracking functionalities within a single system.

The project is developed by an eight-member Scrum team using the Agile Scrum methodology. The development process is divided into four sprints lasting between 7 and 10 days, with each sprint focusing on different system functionalities such as authentication, communication systems, commission workflows, and payment integration. More complex tasks such as escrow payments, notifications, and system testing were planned for longer

1.1 Problem Definition

Many freelance creators (artists, developers, etc.) and clients face severe communication breakdowns, trust issues, and discoverability challenges in custom commission processes. Vague client requests often lead to repeating conversations that lead to nowhere. Additionally, new creators struggle to gain visibility on traditional platforms. Furthermore, the lack of a secure and universal payment ecosystem exposes both parties to fraud, such as catfishing or unpaid labor, making the freelance ecosystem unreliable.

1.2 Background Information

Commissions are formal requests where a client hires a creator to make a custom, one-of-a-kind piece of artwork or product based on specific requirements. The creator economy relies heavily on custom commissions, yet the current workflow is highly fragmented. Creators typically use multiple social media platforms for visibility and to negotiate requirements, and external links for payments. This disjointed approach creates an environment prone to misunderstandings and scams, as none of these platforms offer security for the entirety of the process.

To start with, due to the disjointed approach content creators currently use in case of a scam or other issues that happen during the entire process can not be pinned down to one platform. For example, if a creator uses fake ai images for advertisement in a social media platform but takes payment with a different platform, the buyer cannot demand from any of the two platforms to hold the creator accountable for the scam. Because technically none of the two platforms policies were violated. Another issue is with the vague requests from clients who lack the knowledge to give proper information about their order. As a result, creators are forced to ask or answer the same questions to different clients over and over again, which often leads to misunderstandings and even the client deciding not to place the order. Lastly, using external links for payments can get messy if the client and the creator can not agree on which platform to make the transaction on. Common tools used for transactions by the community in some countries are often unavailable in others, which makes international commissions hard to deal with.

A unified platform that combines a secure social discovery feed, structured order forms that can be customized by the seller, and an escrow-based payment system is essential. By standardizing the request process and securing funds, the platform can eliminate communication chaos and build a trust-based ecosystem for creators.

1.3 Objectives

Trust & Transparency: The platform aims to provide a trustworthy environment for both creators and clients by reducing fraud risks and unauthorized AI-generated content usage. Escrow-based payment protection and structured workflows are designed to increase transparency throughout the commission process.

Communication Efficiency: The system aims to reduce communication complexity by replacing fragmented social media negotiations with structured order forms and integrated messaging systems. This approach helps minimize misunderstandings and repetitive clarification requests between users.

Creator Discoverability: Another objective of the platform is to improve creator discoverability beyond traditional social media searches. Advanced filtering systems and expertise-based tags allow clients to find creators more efficiently according to their specific requirements.

Financial Security: The platform is designed to ensure financial security for all parties involved in commission transactions. Escrow-based payment management protects both creators and clients against unpaid labor, scams, and incomplete deliveries.

Scalability: Bes(t)poke aims to provide a scalable and maintainable software infrastructure capable of supporting a growing creator economy. The modular system architecture allows future feature expansion and easier long-term maintenance.

Advanced Filtering: The system also focuses on implementing advanced filtering functionalities using creator attributes such as category, expertise, price range, and style. These filtering mechanisms help users reach suitable creators more quickly and accurately.

2.0 High-Level Functionality

2.1 Functional Requirements

FR-1: User Registration & Role RBAC

The system must allow users to register with email verification and select either a Creator or Client role. Upon selection, the system must automatically assign a Role-Based Access Control (RBAC) permission set:

- Creators: Access to portfolio management, order form creation, and commission handling tools.
- Clients: Access to discovery, ordering, and payment features.

FR-2: Profile Management

Creators must be able to build public profiles featuring portfolios, pricing, and expertise tags. The system must block the profile from becoming publicly visible until a minimum of 3 expertise tags are configured.

FR-3: Customizable Order Forms

The system must support creator-defined order forms supporting five field types: text input, multiple choice, checkbox, dropdown list, and file upload.(MAX 100MB)

FR-4: Commission Workflow Tracking

The system must provide structured status tracking from initial submission to final delivery. Creators must be able to define a maximum revision limit per order. Once this limit is reached, the system must block further free revision requests and prompt the Client to either accept the current delivery or purchase an additional revision.

FR-5: Escrow Payment Automations

Client funds must be captured and held in a secure escrow system upon order acceptance. The system must release payment to the creator only when:

(a) The client explicitly approves the final delivery

OR

(b) 72 hours pass after the delivery is marked as completed with no dispute raised by the client.

FR-6: Integrated Messaging System

The system must feature an integrated chat system allowing Creators and Clients to communicate both pre-sale and throughout the active commission lifecycle directly inside the application interface.

FR-7: Real-Time Notification Engine

The system must provide a centralized notification engine that automatically dispatches real-time push notifications and alerts to users for critical events, such as order status updates, new messages, and escrow financial actions.

FR-8: Advanced Discovery & Ranking Engine The system must provide a comprehensive discovery platform featuring both manual search filters and automated algorithmic curation. The system must allow Clients to efficiently search and filter Creators using specific parameters (style, category, price range, and expertise tags). Concurrently, the system must feature a backend algorithm that tracks and prominently displays top-performing Creators on the main feed based on cumulative successful project completion rates, average response times, and user ratings.

FR-9: Double-Blind Rating System

The system must support a two-way review and rating workflow upon order completion. Reviews/ratings shall remain hidden and only become publicly visible on profiles when both parties have submitted their review, or after a 7-day period expires.

FR-10: Content & User Reporting System

The system must allow users to report inappropriate profiles, fraudulent behavior, or policy-violating messages within the chat interface. Upon submission, the system must automatically log the incident and flag the reported item in the Admin Dashboard for immediate moderator review and action.

FR-11: Multi-Currency & International Payments

The system must support multi-currency pricing displays (e.g., USD, EUR, TRY) and securely process international credit card transactions to facilitate cross-border commissions.

FR-12: Dispute Resolution Workflow

The system must provide a structured moderator-led conflict resolution process. When a dispute is triggered, the system must automatically:

- (a) Freeze escrowed funds,
- (b) Notify both parties and an assigned moderator,
- (c) Open an evidence-submission window, and
- (d) Allow the moderator to execute a full/partial refund or full release.

2.2 Non-Functional Requirements

NFR-1: System Scalability

The system must support a minimum of 1,000 concurrent active user sessions while ensuring that at least 95% of standard HTTP requests maintain a response time under 2 seconds.

NFR-2: System Performance

The system must deliver advanced discovery search results within 3 seconds and dispatch real-time system notifications within 1 second under standard network conditions.

NFR-3: Data Security & Compliance

The system must enforce end-to-end TLS 1.3 encryption for data in transit, utilize AES-256 encryption for all data at rest, and maintain strict compliance with PCI-DSS standards for all payment transactions.

NFR-4: Platform Availability

The system must guarantee a 99.9% application uptime calculated on a rolling monthly basis, excluding pre-announced and scheduled maintenance windows.

NFR-5: Process Isolation

The system must isolate heavy background tasks such as large file processing and high-volume notification dispatches using dedicated background worker threads to prevent user interface latency or blocking exceeding 2 seconds.

NFR-6: Regulatory Compliance

The system must strictly adhere to GDPR regulations by implementing automated data minimization workflows and providing user-triggered "right to be forgotten" data erasure protocols.

NFR-7: Interface Usability

The system must provide an intuitive interface that allows first-time users to complete and submit a standard custom order flow in a maximum of 5 distinct actions or clicks without requiring external documentation.

NFR-8: Cross-Platform Compatibility

The system must deliver an adaptive responsive layout that renders correctly across Google Chrome, Mozilla Firefox, Apple Safari, and Microsoft Edge, ensuring full client-side script execution completes within 3 seconds.

NFR-9: System Maintainability

The system must utilize a decoupled, modular software architecture ensuring that any future structural component changes or feature enhancements require modifications to less than 20% of the existing core codebase.

NFR-10: System Auditability

The system must maintain an append-only, immutable transaction database layer that logs all financial transitions and status updates using standardized ISO-8601 timestamps for transparent auditing.

3.0 Software Tools

The Bes(t)poke platform requires a carefully selected set of software tools to support its core functionalities, including secure escrow-based payments, AI content detection, real-time messaging, and scalable cloud deployment. Each tool was evaluated based on three

normalized criteria: cost, training time, and functionality. Cost and training scores are inverted (100 minus the raw value) so that lower cost and less training time yield higher scores. The tool with the highest combined total score was selected for each task.

3.1 Deployment Platform — AWS

A cloud deployment platform is required to host the backend services, database, and media storage of the Bes(t)poke platform. The platform must support .NET Core services, MS SQL Server hosting, and content delivery at scale. Three platforms were evaluated: AWS, Google Cloud, and Microsoft Azure. AWS was selected because it provides native support for both .NET Core and MS SQL Server through its RDS (Relational Database Service), while also offering compute, storage, CDN (Content Delivery Network), and SQS (Simple Queue Service) under a single infrastructure. This eliminates integration complexity and reduces deployment risk for our specific technology stack. Its total score of 160.5 outperformed Google Cloud (90.9) and Microsoft Azure (108.8).

Table 3.1 — Deployment Platform Tool Comparison

Criterion	AWS	Google Cloud	Microsoft Azure
Cost (\$/month)	130	160	150
Training Days	7	12	10
Functionality (0-100)	99	90	85
Normalized Scores			
Cost Score	18.8	0.0	6.2
Training Score	41.7	0.0	16.7
Functionality Score	100.0	90.9	85.9
Total Score	160.5	90.9	108.8

3.2 Frontend Framework — [React.js](#)

A frontend framework is required to build the dynamic and interactive user interface of the platform, including the marketplace discovery feed, commission order forms, and

real-time order tracking screens. Three frameworks were evaluated: React.js, Vue.js, and Angular. React.js was selected due to its component-based architecture, which allows reusable UI elements and speeds up development significantly. Its large ecosystem and talent availability further reduce delivery risk. React.js achieved a functionality score of 100.0 and a total score of 258.3, outperforming Vue.js (225.1) and Angular (186.7).

Table 3.3 — Frontend Framework Tool Comparison

Criterion	React.js	Vue.js	Angular
Cost (\$/month)	0	0	0
Training Days	5	8	12
Functionality (0-100)	98	90	85
Normalized Scores			
Cost Score	100.0	100.0	100.0
Training Score	58.3	33.3	0.0
Functionality Score	100.0	91.8	86.7
Total Score	258.3	225.1	186.7

3.3 Backend Framework — .NET Core (ASP.NET Core)

A backend framework is required to handle all server-side logic including user authentication, commission workflow management, escrow payment processing, and dispute resolution. Three frameworks were evaluated: .NET Core, Node.js, and Spring Boot. .NET Core was selected primarily for its built-in LINQ (Language Integrated Query) feature, which allows database queries to be written in C# rather than raw SQL, automatically preventing SQL Injection attacks. This is critical for a platform that handles sensitive financial transactions. Its functionality score of 100.0 and total score of 258.3 outperformed Node.js (214.9) and Spring Boot (186.7).

Table 3.4 — Backend Framework Tool Comparison

Criterion	.NET Core	Node.js	Spring Boot
Cost (\$/month)	0	0	0
Training Days	5	8	12
Functionality (0-100)	98	80	85
Normalized Scores			
Cost Score	100.0	100.0	100.0
Training Score	58.3	33.3	0.0
Functionality Score	100.0	81.6	86.7
Total Score	258.3	214.9	186.7

3.4 Database — MS SQL Server

A relational database is required to store all platform data including user profiles, commission orders, escrow transaction records, and audit logs. Three databases were evaluated: MS SQL Server, PostgreSQL, and Oracle DB. MS SQL Server was selected due to its native compatibility with .NET Core and C#, enabling seamless integration through Entity Framework. Entity Framework automatically translates C# code into SQL queries, making database operations both faster and more secure. This integration is particularly critical for the escrow system, where data integrity and complete transaction logging are mandatory. Oracle DB was eliminated due to its excessive annual cost of \$47,500. MS SQL Server achieved a total score of 231.8, outperforming PostgreSQL (196.1) and Oracle DB (100.0).

Table 3.5 — Database Tool Comparison

Criterion	MS SQL Server	PostgreSQL	Oracle DB
Cost (\$/year)	15,123	12,000	47,500
Training Days	4	6	12
Functionality (0-100)	95	70	98
Normalized Scores			
Cost Score	68.2	74.8	0.0
Training Score	66.7	50.0	0.0
Functionality Score	96.9	71.4	100.0
Total Score	231.8	196.1	100.0

3.5 Payment / Escrow — Iyzico

A payment and escrow provider is required to securely hold client funds during the commission process and release them based on predefined conditions. Three providers were evaluated: Iyzico, PayTR, and Stripe. Iyzico was selected because it is fully compatible with Turkish financial regulations and provides a developer-friendly API for escrow-style transaction flows. Client funds are held with Iyzico until the client explicitly approves the delivery or 72 hours pass without a dispute. In case of a dispute, funds are instantly frozen until a moderator issues a resolution. Additionally, Iyzico handles PCI-DSS compliance on behalf of the platform, eliminating the need to store sensitive card data directly. Iyzico achieved a total score of 125.0, outperforming PayTR (96.2) and Stripe (114.7).

Table 3.6 — Payment / Escrow Tool Comparison

Criterion	Iyzico	PayTR	Stripe
Cost (Commission %)	2.9	2.5	2.9
Training Days	3	4	2
Functionality (0-100)	85	70	55
Normalized Scores			
Cost Score	0.0	13.8	0.0
Training Score	25.0	0.0	50.0
Functionality Score	100.0	82.4	64.7
Total Score	125.0	96.2	114.7

4.0 Software Process Model

Table 4.1 — Product BackLog Items

#	Product BackLog
1	Database Planning
2	Allow users to sign up and log in.
3	Allow users to create public profiles featuring portfolios, pricing, and mandatory expertise tags.
4	Enable clients to browse through creator profiles.
5	Enable users to search for creators and filter by price,tags etc.
6	Let users create creator-defined order forms.
7	Let users create creator-defined revision forms.
8	Enable users to place orders.
9	Enable users to demand revisions.
10	Enable creators and clients to communicate through a in-app chat system.
11	Process payments securely using an escrow based payment provider.
12	Track commisions, display commision history, and manage commision statuses.
13	Create a two-way review and rating system.
14	Create a report system.
15	Provide administrative controls to manage accounts, disputes, and reports.
16	Ensure the website is optimized with an engaging user interface.
17	Implement a notification system.
18	Complete system testing.

The software process model of the project is SCRUM. This framework was chosen due to its agile nature which increases the delivery speed and allows room for changing requirements. The SCRUM team consists of eight members. The product owner is Berk Mertoğlu. He will be creating and managing the product backlog. The scrum master is Arzum Naz Güney. The developers of the team are Atakan Coşar, Zeynep Durmuş, Aslı ARAS, Ata Barış Kuğu, Berkay KOÇ, Eralp Çolakoğlu. The development period is divided into four sprints that vary in length from one to two weeks. The product backlog items are distributed between these sprints according to their level of importance and the dependencies between them. Each one has a sprint goal that focuses on a specific functionality the final product must have.

Table 4.2 — Sprint 1

STAFF	ACTION	STATUS	PRIORITY	START	FINISH	DURATION (DAYS)	NOTES AND COMMENTS
All developers, Product Owner(Berk Mertoğlu)	Database Planning	In Progress	High	4.09.2028	6.09.2028	3	A robust database is the central, structured repository that efficiently stores, organizes, and secures all critical application data.
All developers	User Registration and Authentication	Ready to Start	High	7.09.2028	7.09.2028	1	Sign-up/login with role selection.
All developers	User Profile Creation/Management	Ready to Start	High	8.09.2028	8.09.2028	1	Allow access to different permission sets according to the chosen role, let the creators upload their portfolios
All developers	Responsive Design & UX Enhancements	Not Started	Medium	11.09.2028	12.09.2028	2	Ensure mobile-friendly layout, improved UX.
						9	

During sprint one, first all developers along with the product owner will be working on database planning, as a robust database is the central, structured repository that efficiently stores, organizes, and secures all critical application data and therefore directly affects the entire structure of the project. Next, user registration and authentication functionality, which allows users to sign in and out of the system with role selection will be implemented. Subsequently, the team will work on user profile creation and management that must allow access to different permission sets according to the chosen role of the user. The last sprint backlog item is to ensure the website' user interface is optimized with a responsive design and UX enhancements. This sprint is expected to last 9 days and by the end of the sprint, it is expected for a simple system that allows users to sign in and out of, and manage their profiles to be obtained.

Table 4.3 — Sprint 2

STAFF	ACTION	STATUS	PRIORITY	START	FINISH	DURATION (DAYS)	NOTES AND COMMENTS
All Developers	Creator Portfolio Browsing	Not Started	High	13.09.2028	14.09.2028	2	Display the profiles of the top creators.
All Developers	Creator Search with tags & Filter	Not Started	Medium	14.09.2028	15.09.2028	2	Include keyword search; category,price etc. filter.
Atakan,Ashl, Eralp	Custom Order Form Creation	Not Started	Medium	19.09.2028	19.09.2028	1	Creator-defined order forms with multiple field types(e.g., text input, multiple choice, checkbox, dropdown list, and file upload (max 20MB))
Zeynep,Berkay,Ata	Custom Revision Form Creation	Not Started	Medium	20.09.2028	20.09.2028	1	Creator-defined revision forms with multiple field types(e.g., text input, multiple choice, checkbox, dropdown list, and file upload (max 20MB))
All Developers	Order Placement	Not Started	High	21.09.2028	22.09.2028	2	Allow users to fill the order forms(custom or default) and place their order.
All Developers	Order Revision	Not Started	High	25.09.2028	26.09.2028	2	Allow users to fill the revision forms(custom or default) and demand changes.
						14	

Moving on to the second sprint, the sprint goal is to allow users to be able to go through the entire process of placing their order,except for the payment step. First, the users will be enabled to browse through creator profiles by displaying the profiles of the top creators. Next, the users will be enabled to search for creators fitting for their requirements by searching for them with tags and filters. Subsequently, the functionality to allow users with the “creator” role to create their own custom order forms will be implemented. Concurrently, the same process will be repeated for custom revision forms. Lastly, the functionality to allow users with the “customer” role to fill the custom order and revision forms to place their orders will be implemented. The sprint duration is expected to be 14 days and at the end of the sprint, it is expected for each sprint backlog item including the sprint goal to reach the definition of done.

Table 4.4 — Sprint 3

STAFF	ACTION	STATUS	PRIORITY	START	FINISH	DURATION (DAYS)	NOTES AND COMMENTS
All Developers	Chat System	Not Started	Medium	27.09.2028	28.09.2028	2	Allows for clear communication between the client and the creator.
All Developers	Order status tracking system	Not Started	High	29.09.2028	3.10.2028	3	Track commission status/history, revision count
All Developers	Two-way Review,Rating & Report System	Not Started	Medium	4.10.2028	5.10.2028	2	Both the clients and creators can post reviews and ratings after the commission process is finished.
						9	

In the third sprint, the sprint goal is to allow users to clearly communicate with other users with either role, except for admin, before, during and, after an order has been placed and fulfilled. The first sprint backlog item is implementing an in-site chat system that users with any role can send texts, audios and images as messages to other users as seen on FR-6 in the section 2.1 Functional Requirements. Next item is the creation of an order status tracking system that can be updated by the creators and seen by the customers. This system also must

keep track of all the information about the already completed orders and make it available for both sides. Lastly, a two way blind review, rating & report system, which's specifications have already been discussed in the section 2.1 Functional Requirements as FR-9 and FR-10. The sprint is expected to be 9 days.

Table 4.5 — Sprint 4

STAFF	ACTION	STATUS	PRIORITY	START	FINISH	DURATION (DAYS)	NOTES AND COMMENTS
All Developers	Chat System	Not Started	Medium	27.09.2028	28.09.2028	2	Allows for clear communication between the client and the creator.
All Developers	Order status tracking system	Not Started	High	29.09.2028	3.10.2028	3	Track commission status/history, revision count
All Developers	Two-way Review, Rating & Report System	Not Started	Medium	4.10.2028	5.10.2028	2	Both the clients and creators can post reviews and ratings after the commission process is finished.
						9	

The fourth and last sprint's backlog includes all of the remaining product backlog items. The first item is to integrate the escrow based payment gateway to secure the payment processing. Details on this item have already been given in the section 2.1 Functional Requirements as FR-5. The second item is the creation of the admin dashboard, which will allow moderators, users with the admin role, to manage accounts, disputes, and reports. The next item in the sprint backlog is to implement a notification system. The specifications of this system have already been explained in the section 2.1 Functional Requirements as FR-7. Lastly, the testing of the complete system will be done near the end of this sprint to guarantee that all product backlog items have reached the definition of done and fulfill the current functional and non-functional requirements. This sprint is expected to span 11 days and by the end of the sprint it is expected to obtain a fully-functional and optimised website.

The contents of the sprint backlogs are susceptible to change depending on the results of the previous sprint review and retrospective. This is necessary to allow room for changing requirements and to ensure the quality is up to standard.

5.0 Schedule and Effort

The project schedule was planned using a sprint-based approach. The development process is divided into four main sprints, and each sprint focuses on a specific group of system features. This structure allows the team to organize the workload more clearly, follow the project progress step by step, and manage deadlines more effectively.

In the first sprint, the main focus is on basic system setup and essential user-related features. This stage creates the foundation of the system and prepares the project for later development steps. In the second sprint, creator-related and order-related features are planned. These features are important because they support the main interaction between customers and creators. The third sprint focuses on communication and order tracking features, which help users follow the progress of their requests and communicate within the platform. Finally, the fourth sprint includes payment, admin panel, notification features, and testing activities. These tasks are placed in the final sprint because they require more integration, security checks, and system validation.

Effort planning was also considered while preparing the schedule. High-effort tasks, such as payment integration, admin panel development, notifications, and testing, require more time, coordination, and careful review. Therefore, these tasks were planned carefully in the schedule to reduce project risks and avoid delays. Lower-effort or foundational tasks were placed earlier in the project so that the team could build the system gradually. Overall, the schedule supports a step-by-step development process and helps balance the workload among team members.

ALL	TASK NAME	DURATION	PLANNED STA...	PLANNED FINIS...	LINKED F...	+
1	Sprint 1	7 days	4.09.2026	14.09.2026		
2	Database Planning	3 days	4.09.2026	8.09.2026		
3	User Registration a...	1 day	9.09.2026	9.09.2026	2	
4	User Profile Creatio...	1 day	10.09.2026	10.09.2026	3	
5	Responsive Design & U...	2 days	11.09.2026	14.09.2026	4	
6	Sprint 2	7 days	15.09.2026	23.09.2026		
7	Creator Portfolio Br...	2 days	15.09.2026	16.09.2026		
8	Creator Search & Fil...	2 days	17.09.2026	18.09.2026	7	
9	Custom Order Form ...	1 day	21.09.2026	21.09.2026	8	
10	Custom Revision Fo...	1 day	21.09.2026	21.09.2026	8	
11	Order Placement	2 days	22.09.2026	23.09.2026	9	
12	Order Revision	2 days	22.09.2026	23.09.2026	10	
13	Sprint 3	7 days	24.09.2026	2.10.2026		
14	Chat System	2 days	24.09.2026	25.09.2026		
15	Order Status Tracki...	3 days	28.09.2026	30.09.2026	14	
16	Two-Way Review, R...	2 days	1.10.2026	2.10.2026	15	
17	Sprint 4	8 days	5.10.2026	14.10.2026		
18	Escrow Based Paym...	2 days	5.10.2026	6.10.2026		
19	Creating Admin Panel	2 days	7.10.2026	8.10.2026	18	
20	Notification System	1 day	9.10.2026	9.10.2026	19	

Figure 5.1 — Project Schedule

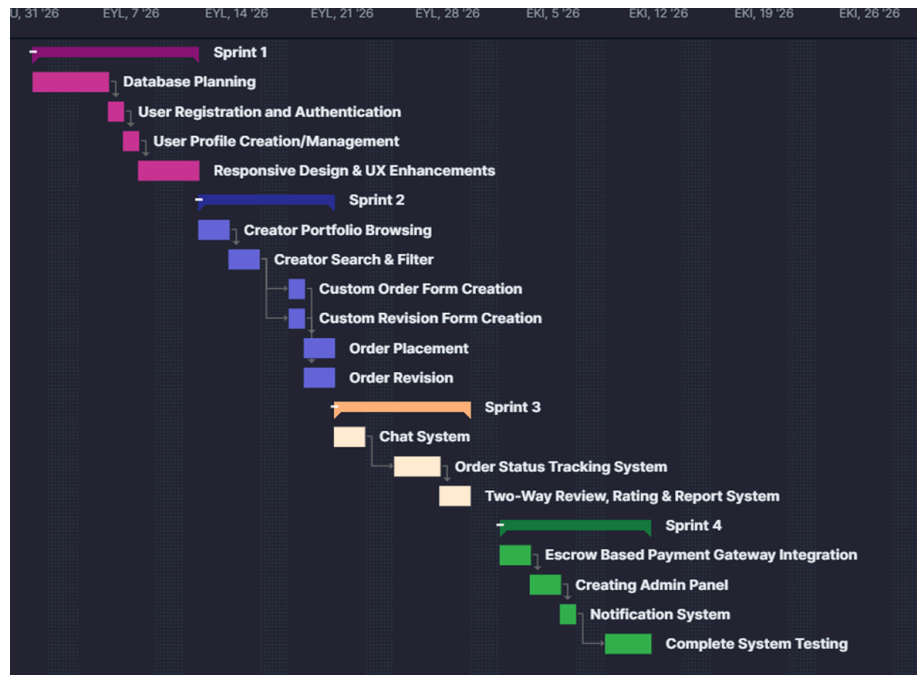


Figure 5.2 — Project Schedule Gantt Chart

6.0 Stakeholders and Project Risks

6.1 Stakeholders

Table 6.1 — Stakeholders

#	STAKEHOLDERS
1	Developer Team
2	End User
3	Competitors
4	Bank and Paygate Providers
5	Sponsors and Investors
6	T.C. Ministry of Commerce
7	Customers
8	Administrative Staff

The developer team is responsible for designing, coding, testing, and maintaining the Bes(t)poke platform. They contribute directly to the technical development of the system, including payment integration, messaging features, database management, and user interface implementation. If the project becomes successful, the developers will improve their technical skills, gain professional experience, and increase their credibility in the software industry. In case of project failure, they may lose valuable time, motivation, and professional reputation after investing significant effort into the development process.

End users are the people who directly interact with the platform and use its services. They contribute to the growth and success of the system by using the platform for communication,

secure transactions, portfolio discovery, and commission management. If the project succeeds, users will benefit from a secure, organized, and trustworthy commission ecosystem. However, if the platform fails, users may experience financial losses, security concerns, poor user experience, or difficulties finding reliable creators and clients.

Competitors indirectly contribute to the project by encouraging innovation and motivating the team to improve the platform continuously. Their presence increases market competition and pushes the project to offer better functionality, security, and user experience. If the project becomes successful, competitors may lose market share and users to the Bes(t)poke platform. On the other hand, if the project fails, competitors may maintain their dominance in the market without losing users or revenue.

Banks and payment providers such as Iyzico provide the financial infrastructure required for secure transactions and escrow-based payments. Their systems allow users to complete international payments safely and support the financial reliability of the platform. If the project succeeds, these providers may process higher transaction volumes and improve their reputation through partnership with a successful platform. If the project fails, they may lose potential revenue opportunities and business growth related to the platform.

Sponsors and investors provide the financial resources needed for software development, infrastructure, deployment, and maintenance. Their support allows the team to continue development activities and improve system quality. In case of project success, they may gain financial profit, stronger market reputation, and future investment opportunities. However, if the project fails, they may lose their financial investment, development resources, and professional time spent supporting the project.

The Ministry of Commerce establishes legal regulations related to digital commerce, online transactions, and data privacy laws. These regulations directly affect the structure and compliance requirements of the platform. Although the government does not directly profit from the project's success, a successful platform may contribute positively to the digital economy and secure online commerce ecosystem. If the project fails, the impact on the government would remain limited because it mainly acts as a regulatory authority.

Customers use the platform to request custom services, communicate with creators, and complete secure commission transactions. Their participation is essential for maintaining platform activity and generating revenue. If the project succeeds, customers will benefit from a secure, transparent, and organized commission process with reduced fraud risk. If the project fails, customers may lose trust in the platform, experience payment-related problems, or face risks related to scams and insecure transactions.

Administrative staff are responsible for moderating the platform, reviewing reports, resolving disputes, and maintaining platform order. They contribute to the security and reliability of the system by ensuring that users follow platform policies and community guidelines. If the project succeeds, administrative staff will maintain stable employment and continue managing the platform. If the project fails, their positions and responsibilities within the system may no longer be necessary.

6.2 Project Risks

Table 6.2 — Risk Analysis Matrix

LIKELIHOOD RANK	IMPACT RANK	COMBINED RANK	RISK DESCRIPTION
1	2	3	Uncertain Requirements
2	3	5	Time Management Issues
5	1	6	Payment Restrictions
4	4	8	Departure of Developer
3	6	9	Training Time
6	7	13	Issues Within Team
8	5	13	Insufficient Testing
7	8	15	Inadequate Equipment

Uncertain Requirements: This risk refers to the possibility that the requirements defined by the client may not be fully clear at the beginning of the project or may change during development. The likelihood rank is 1 because changing requirements are very common in software development projects, especially in systems with many features and user interactions. The impact rank is 2 because unclear requirements can cause redesign, additional workload, communication problems, and project delays. The combined rank of 3 indicates that this is one of the most critical risks in the project and requires continuous communication and careful requirement management.

Time management issues: Time management issues may occur if the development team underestimates the time required for coding, testing, or integration tasks. The likelihood rank is 2 because scheduling problems are common in team-based software projects. The impact rank is 3 because delays may affect sprint planning, project deadlines, and overall delivery quality. The combined rank of 5 shows that proper planning and task distribution are important for maintaining project progress.

Payment Restrictions: The platform depends heavily on payment gateways and escrow systems for secure transactions. Restrictions, legal limitations, or the withdrawal of payment providers may negatively affect the financial infrastructure of the platform. The likelihood rank is 5 because payment systems are generally stable but external restrictions may still occur. The impact rank is 1 because payment integration is one of the core functionalities of the system, and losing it would seriously affect platform operations. The combined rank of 6 demonstrates that this risk has a very high business impact despite its lower probability.

Departure of Developer: A developer leaving the team unexpectedly may create a loss of technical knowledge and increase the workload of the remaining team members. The likelihood rank is 4 because team changes may happen during long development periods. The impact rank is 4 because losing a developer can slow development, reduce productivity, and

delay important tasks. The combined rank of 8 shows that documentation and teamwork are necessary to reduce dependency on individual developers.

Training Time: The project requires modern frameworks, APIs, cloud services, and deployment platforms that some team members may not fully understand initially. The likelihood rank is 3 because learning new technologies is common during software development. The impact rank is 6 because additional learning time may slow development speed and affect sprint progress during the early stages of the project. The combined rank of 9 indicates that technical preparation and training are important for efficient development.

Issues Within Team: Communication problems, role conflicts, or personal disagreements between team members may reduce productivity and negatively affect project coordination. The likelihood rank is 6 because teamwork problems are not uncommon in group projects. The impact rank is 7 because poor communication can delay tasks, reduce software quality, and create management difficulties. The combined rank of 13 shows that maintaining effective communication and teamwork is necessary for project success.

Insufficient Testing: The team may not be able to test all possible scenarios due to limited time, resources, or testing data. The likelihood rank is 8 because testing is already included as part of the development process and major testing failures are less likely. The impact rank is 5 because insufficient testing may leave software bugs, usability issues, or security vulnerabilities unresolved in the final product. The combined rank of 13 indicates that although this risk is less likely, it can still negatively affect software quality if not managed properly.

Inadequate Equipment: Limited hardware, software resources, or technical infrastructure may slow down development, testing, and deployment activities. The likelihood rank is 7 because modern development tools are generally accessible to the team. However, the impact rank is 8 because technical limitations can still reduce development efficiency and system performance.

The combined rank of 15 shows that this is one of the lower-priority risks in the project, but it may still affect development quality if proper resources are unavailable.

7.0 Measurements

Table 7.1 — Measurements

Measurement Type	Description	Example Measurements
Schedule	Tracks development and documentation hours spent each week	45 staff-hours spent in Week 5.
Product Size	Measures the scale of the product in terms of object points and person-months using COCOMO 2	$\text{NOP} = [24 \times (100-10)] / 100 = 21.6 \text{ NOP}$ $21.6/7 = 3.086 \text{ person-month}$
Quality	Tracks the total number of bugs found during testing sessions.	6 defects found in the registration module.
Change	Measures how many times requirements were updated.	2 major requirement changes during the analysis phase

Schedule: This type of measurement focuses on tracking the hours spent on development and documentation each week to keep the project's schedule on track. As part of process management, the planned and actual weekly working hours for each milestone are closely tracked. The weekly work data collected is securely stored by all team members at the end of each week by entering it into a shared project spreadsheet as person-hours. According to the project's schedule and effort tracking, a total of 45 person-hours were spent in Week 5.

Product Size: This type of measurement aims to verify the scale of a software product using the COCOMO 2 model, based on object points and person-months. The metrics defined

within the model include COCOMO 2 object points calculated by taking complexity weights and the related person-month parameters. Technical size of the project, before the start of development as object points and person-months with complexity weight by calculating with COCOMO 2 and recording in an Excel file. According to preliminary calculations the scale of the project was found as “ $NOP = [24 \times (100-10)]/100 = 21.6 \text{ NOP}$ ” and effort requirement was calculated as “ $21.6/7 = 3.086 \text{ person-month}$ ”.

Quality: This type of metric that measures the project’s stability is used to track the total number of bugs identified during the test sessions. The identified measurement of quality processes is the number of defects found per test conducted across the system. After each integration is completed, the number of defects detected per test is calculated based on data collected from the GitHub error log as an integer. To give an example of existing records related to quality tracking, six errors were identified during testing in the registration module that is one of the system’s critical components.


Change: This measurement type verifies how many times requirements were updated and revised throughout the process in order to assess the stability of the project’s scope. The total number of changes made directly to the software requirements is recorded as part of the measurement. Number of changes in the requirements, after each sprint review, in integer format gathered by team members and listed in an Excel file and kept in the past versions of the project. According to the data collected regarding change management, two major changes in requirements occurred during the analysis phase that constitutes the early stages of the project.

8.0 Graphical User Interfaces


8.1 Customer's Interfaces

8.1.1 Homepage

This home page allows guest users to discover creators and their services through categorized searches and spotlights, without requiring any account login. Customers can sign up using the 'Register' button, while creators can register by clicking 'Become a Seller'.

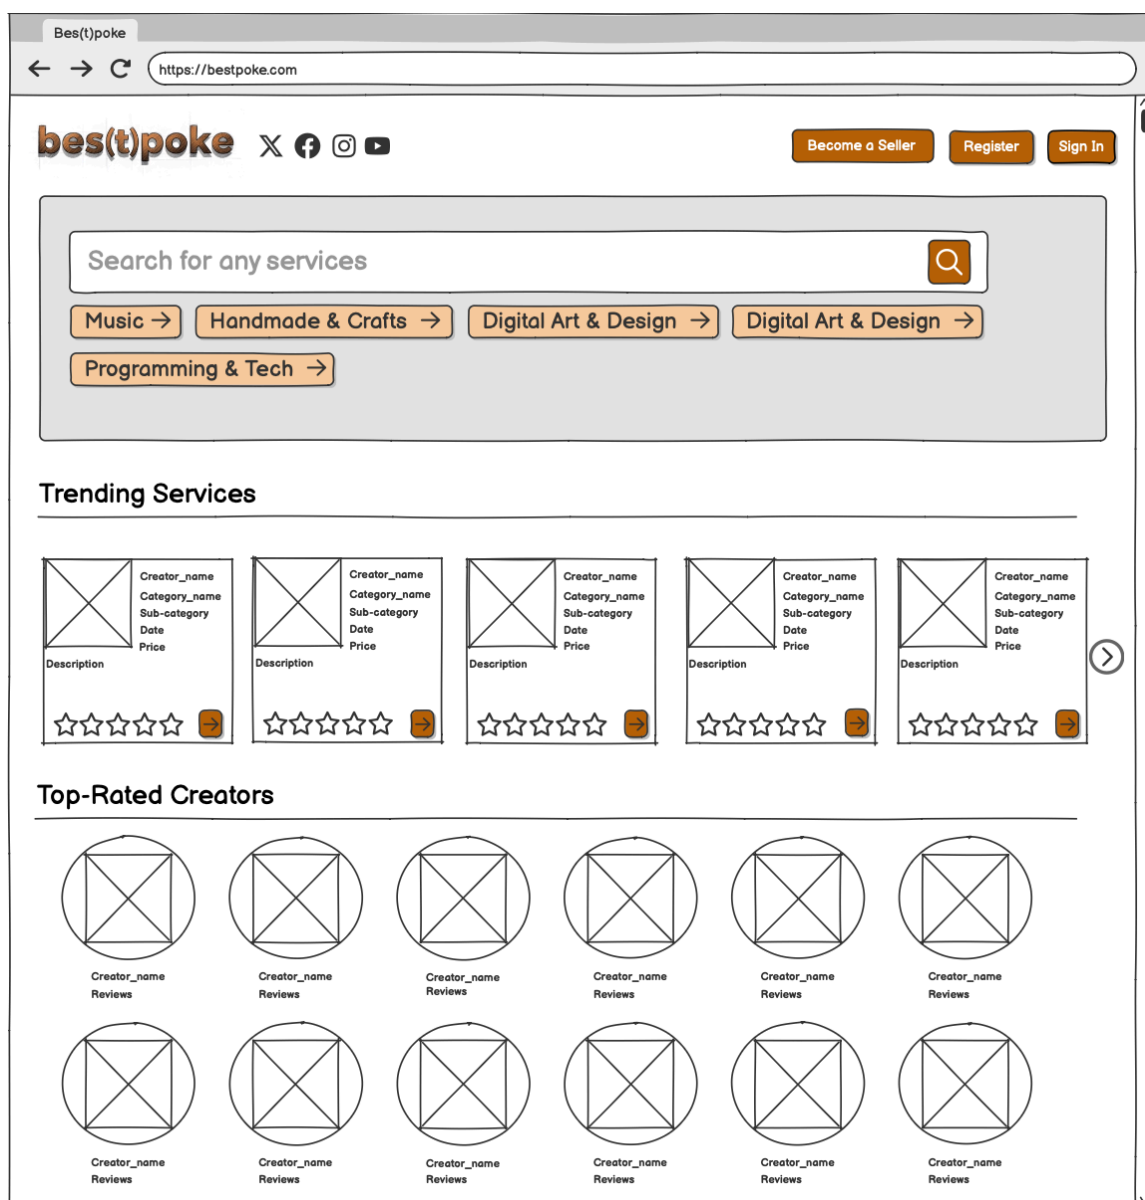

8.1.2 Customer Registration Page

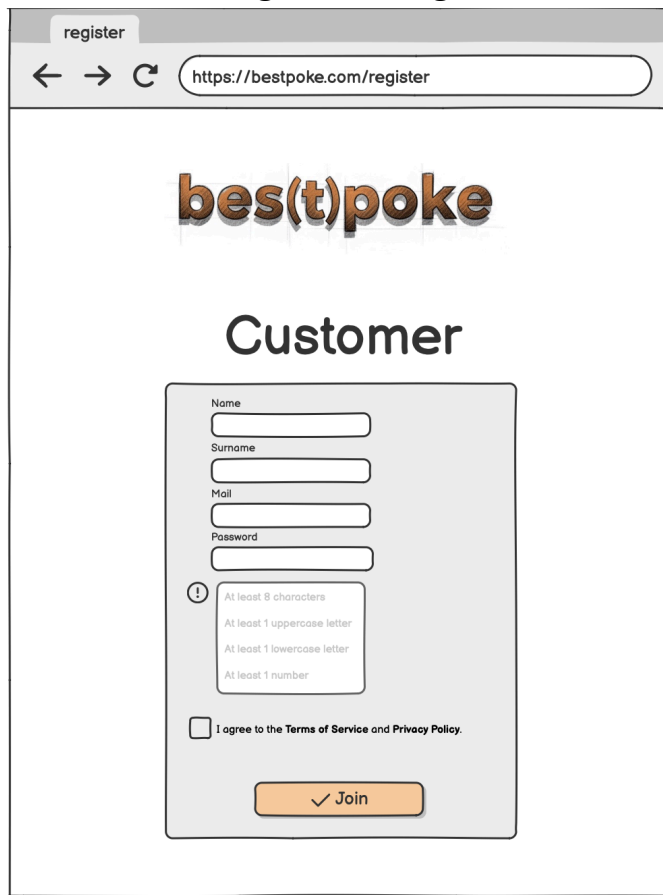

The registration page features a browser window with the address bar showing 'https://bestpoke.com/register'. The page has a 'register' tab and the 'bes(t)poke' logo. Below the logo is the heading 'Customer'. The registration form includes fields for Name, Surname, Mail, and Password. A password strength indicator shows requirements: at least 8 characters, 1 uppercase letter, 1 lowercase letter, and 1 number. There is a checkbox for 'I agree to the Terms of Service and Privacy Policy' and a 'Join' button.

register

← → ↻ https://bestpoke.com/register

bes(t)poke

Customer

Name

Surname

Mail


Password

ⓘ At least 8 characters
At least 1 uppercase letter
At least 1 lowercase letter
At least 1 number

☐ I agree to the Terms of Service and Privacy Policy.

✓ Join

8.1.3 Customer Sign-In Page

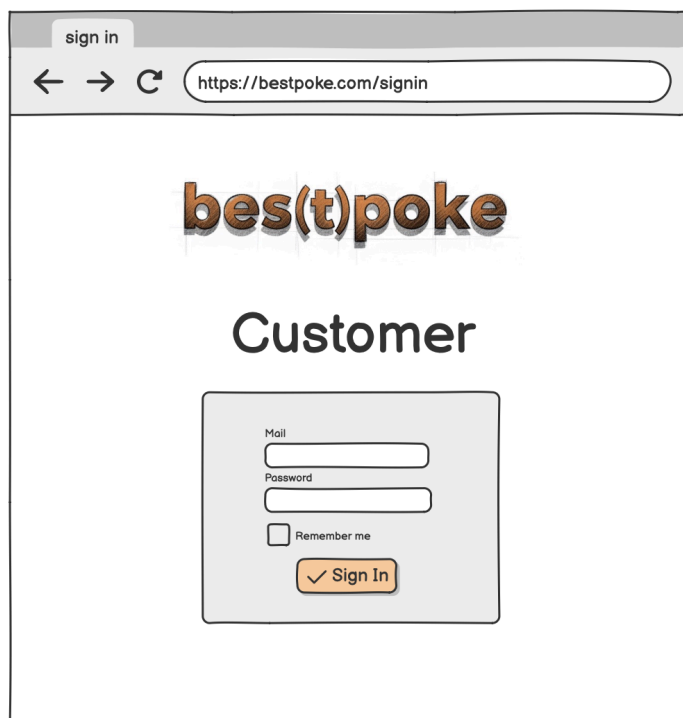

The sign-in page features a browser window with the address bar showing 'https://bestpoke.com/signin'. The page has a 'sign in' tab and the 'bes(t)poke' logo. Below the logo is the heading 'Customer'. The sign-in form includes fields for Mail and Password, a 'Remember me' checkbox, and a 'Sign In' button.

sign in

← → ↻ https://bestpoke.com/signin

bes(t)poke

Customer



Mail

Password


☐ Remember me

✓ Sign In


8.1.4 Customer Home Page

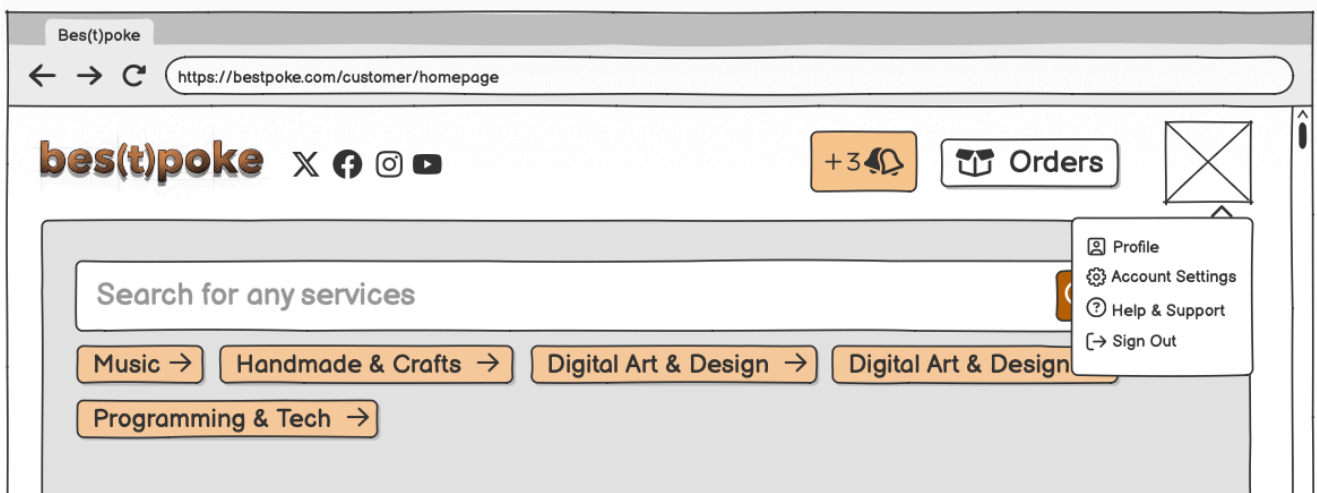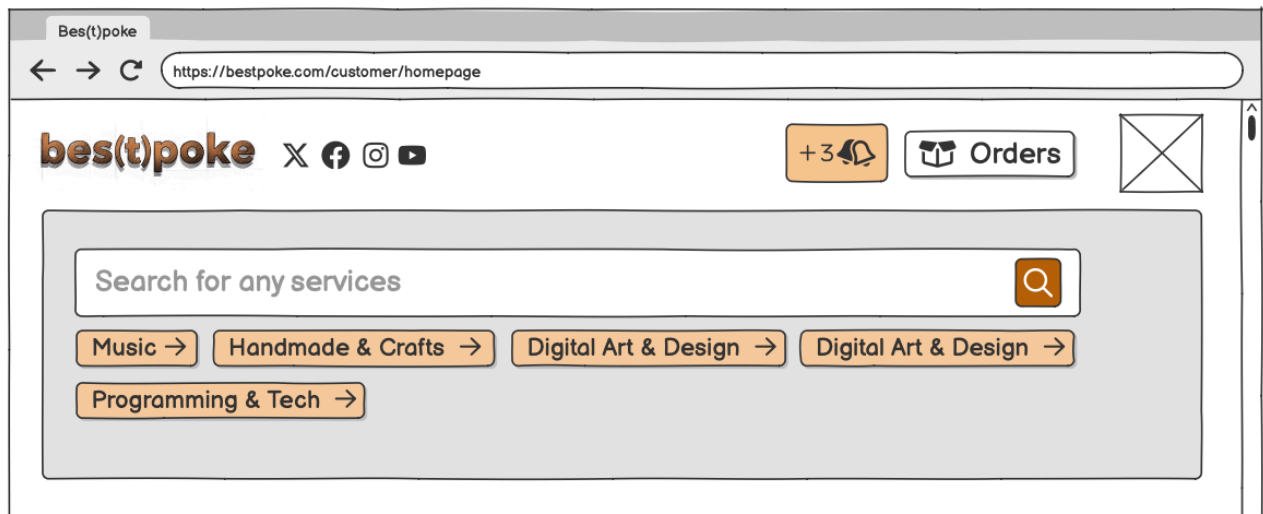

Trending Services



Top-Rated Creators

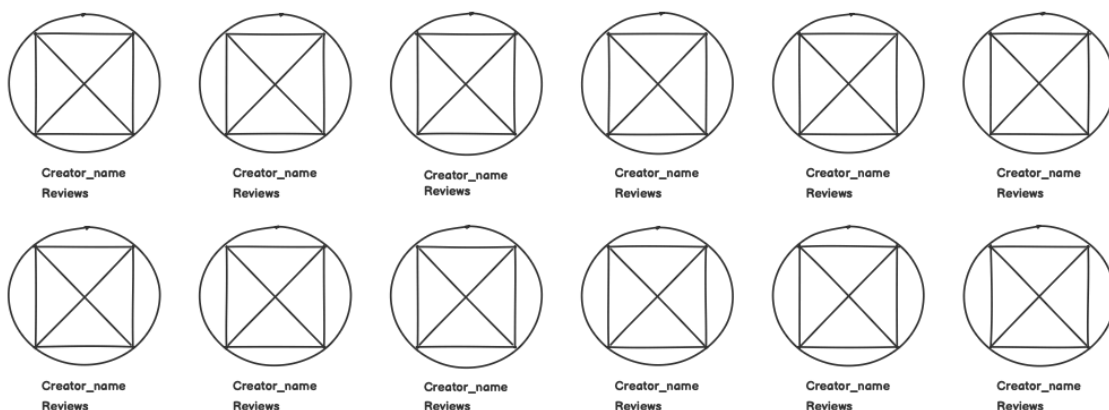

From this page, users can obtain information about the creator. If this information is sufficient, they can proceed to the form completion section created by the creator through the 'Request Commission' form part. However, if they are unsure, they can click on the 'Works' section to examine the creator's other works.

Bes(t)poke/creator/profile

https://bestpoke.com/customer/creator/profile

bes(t)poke

Xf@v

Contact With

Works

4.2-star rating

AI Shield Active

Creator Details

Name & Surname:
Creator_name&surname

Mail:
Creator_mail

Addres:
Creator_addres

Social Media

@in

Biography

Expertise

SongWriter

Pop

Music Composition

Ambient

Certificates

Request Commission Form

8.1.8 Creator's Previous Works

After reviewing the creator's previous works from this page, if the customer is convinced that the creator can fulfill their order, they can click 'Start Commission Form' to proceed to the form completion section.

The screenshot displays a web browser window with the URL `https://bestpoke.com/creator/works`. The page header includes the **bes(t)poke** logo and social media icons. The main heading is **Creator_name's WORKS**.

On the left, there is a placeholder for a profile picture (a square with an 'X'). To its right, the creator's information is listed:

- Creator_name
- Expertises: #-----, #-----, #-----
- Rating: ☆ ☆ ☆ ☆ ☆ --/5
- Reviews: --

On the right side, there is a button labeled **Start Commission Form** with a document icon.

The main content area contains three placeholder boxes for previous work details, each titled **Product Details**. Each box includes:

- A placeholder for a product image (a square with an 'X').
- A label **Description:** followed by a text input field.
- A **Tags** section with three input fields.
- Labels for **Date:**, **Completion Time:**, and **Price:**, each followed by a text input field.

8.1.9 Creator's From Example

These forms are prepared by the creators. After this form is filled out and 'Submit Request Form' is clicked, the form is sent to the creator's chatbox, thereby starting the communication between the creator and the customer through the chatbox. The purpose of this page is to accelerate the communication between them, make it easier for customers to clarify their requirements, and provide a preliminary project draft for the creator.

×

Submit Custom Music & Audio Order

Project Request:

Descriptive Project Title:

Select Music Genre:

🔧 Ambient

Electronic

Lo-fi

Rock

Ambient

Orchestral

Required Instrument Sounds:

☐ Key / Piano ☐ Acoustic Guitar ☐ Drum ☐ Electric Guitar

File upload

 Upload Reference Tracks/Demos (WAV/MP3)

Detailed Project Description and Vibe:

Estimated Budget Range & specify exact amount:

Desired Completion Date:

/ /

Submit Request Form

8.1.10 Customer Chat Box

From this section, users can communicate with creators, upload documents, and track the current stage of the project. If the status changes to 'Ready for Payout', the payment button turns green and becomes active.

Q Creator_name	
☐ 	 Creator_name online Price: \$ -- Pay  Status: Ready for Payout
☒  Creator_name 	 
☐  Creator_name	
☐  Creator_name	

8.1.11 Escrow Payment Page via Iyzico

This page displays the order summary including the escrow amount, where users can complete their secure transaction via the Iyzico gateway after agreeing to the Escrow Agreement.

bes(t)pokeHome About Contact

Order Summary
Project: Custom Illustration
Base Price: \$150
Iyzico Processing Fee: \$4.50
Total Escrow Amount: \$154.50

Secured by
Iyzico

Cardholder Name

Card Number

Expiry Date

CVV

☐ I agree to the Escrow agreement (Funds held until approval)

Complete Secure Payment

←

8.1.12 Customer Order Page

After a payment is successfully processed, the order appears under the 'Active' orders tab. Additionally, customers can access this page by clicking the 'Orders' button on the homepage to track and review their active or past orders.

Bes(t)poke/customer/orders

← → ↻

https://bestpoke.com/customer/orders

bes(t)poke

X f i y

Active

Delivered

Completed

Cancelled

Orders Name

Order Id: order_id

Order date: order_date

Creator: creator_name

Item: item_name

View Order

Creator Profile

\$ 250

Orders Name

Order Id: order_id

Order date: order_date

Creator: creator_name

Item: item_name

View Order

Creator Profile

\$ 100

Orders Name

Order Id: order_id

Order date: order_date

Creator: creator_name

Item: item_name

View Order

Creator Profile

\$ 25


8.1.13 Customer Profile

This page allows customers to view their current profile details and update information such as name, phone number, address, and social media links by clicking the 'Update' button.

Bes(t)poke/customer/profile

← → ↻ https://bestpoke.com/customer/profile

bes(t)poke X f i y +3 🔔



- 📦 Orders
- ⚙️ Account Settings
- 🔍 Help & Support
- 🚪 Sign Out

Customer Information

Name & Surname:
Customer_name&surname

Mail:
Customer_mail

Phone:
Customer_phone

Addres:
Customer_addres

Social Media
📷

Name & Surname:

Name

Surname

Phone:

+() 555 555 5555

Addres:


Social Media

+

Update

8.1.14 Account Settings Page


On this screen, users can update their core account configurations, including security credentials, email/SMS notification preferences, and saved credit cards.

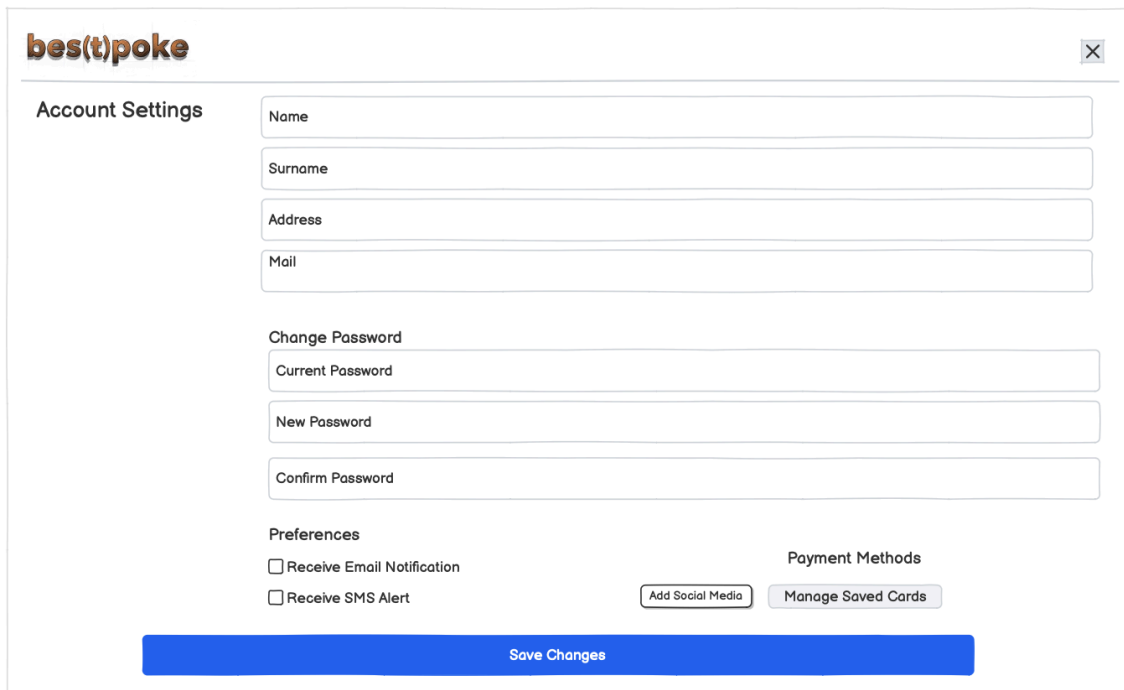

The screenshot shows the 'Account Settings' page for 'bes(t)poke'. The page has a header with the logo and a close button. The main content area is titled 'Account Settings' and contains several sections: 'Personal Information' with fields for Name, Surname, Address, and Mail; 'Change Password' with fields for Current Password, New Password, and Confirm Password; 'Preferences' with checkboxes for 'Receive Email Notification' and 'Receive SMS Alert'; and 'Payment Methods' with buttons for 'Add Social Media' and 'Manage Saved Cards'. A large blue 'Save Changes' button is at the bottom.

8.1.15 Help and Support Page

This page provides solutions through a Frequently Asked Questions (FAQ) section and allows users to report platform issues or payment disputes by opening a support ticket.

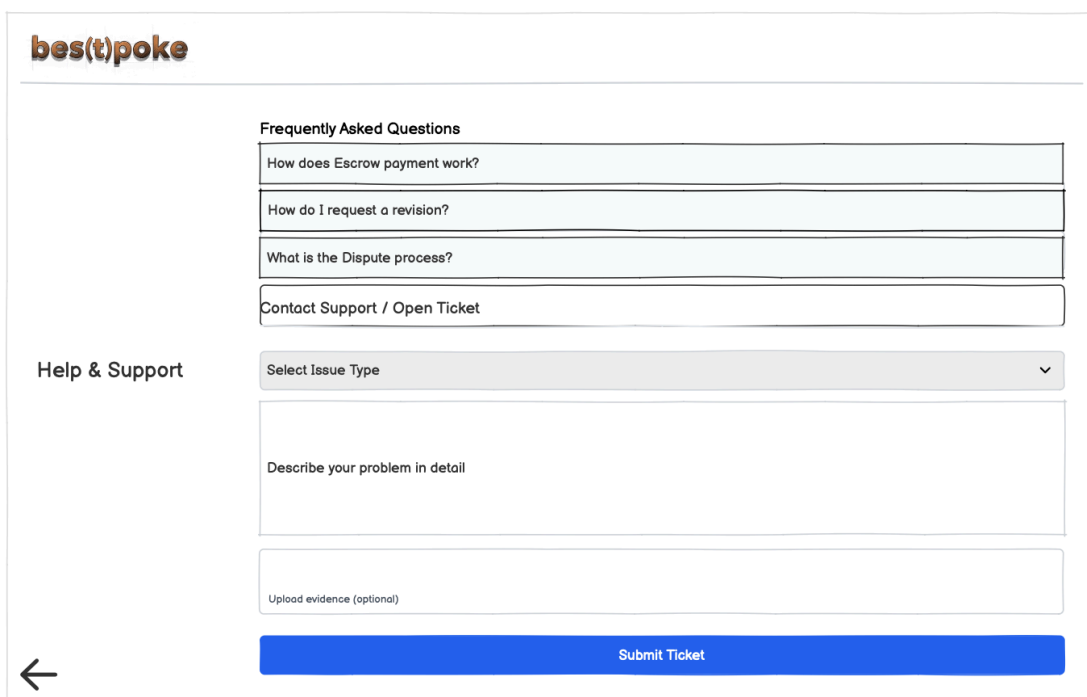

The screenshot shows the 'Help & Support' page for 'bes(t)poke'. The page has a header with the logo. The main content area is titled 'Help & Support' and contains a 'Frequently Asked Questions' section with four questions: 'How does Escrow payment work?', 'How do I request a revision?', 'What is the Dispute process?', and 'Contact Support / Open Ticket'. Below this is a 'Select Issue Type' dropdown menu, a text area for 'Describe your problem in detail', and an 'Upload evidence (optional)' button. A large blue 'Submit Ticket' button is at the bottom. A back arrow is visible in the bottom left corner.

8.1.16 Active Order Tracking

This page serves as a more detailed and advanced version of the tracking interface within the chat section. While the standard chat section is designed for casual communication and general inquiries, this interface formalizes the ongoing discussion and modifications regarding the actual product. Here, the dialogue directly targets scope adjustments and product revisions; users can comprehensively monitor real-time progress through a dynamic status tracking bar, review commission details, and either finalize the contract using 'Accept Delivery' or execute formal changes via 'Request Revision'.

bes(t)poke

HomeOrdersProfile

1

Order Placed

2

In Progress

3

In Review

4

Completed

Commission Details

The initial request was for a detailed illustration of a fantasy landscape, featuring a towering castle on a hill, a winding river, and a mystical forest under a twilight sky. The style should be semi-realistic with a touch of whimsy.

Revisions Remaining: 1

Accept DeliveryRequest Revision

Client message text here.

Client message text here.

Creator message text here.

Creator message text here.


Type a message...Send

←

8.2 Creator's Interfaces


8.2.1 Creator Registration Page

If users click on 'Become a Seller', the registration section for creators opens.

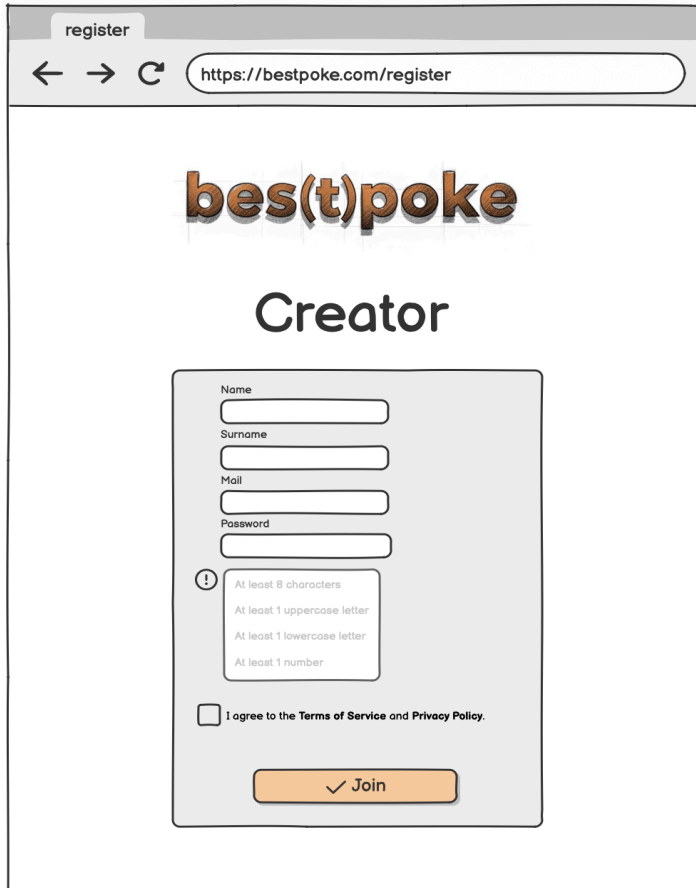


The screenshot shows a web browser window with the address bar displaying "https://bestpoke.com/register". The page features the "bes(t)poke" logo and the title "Creator". The registration form includes fields for Name, Surname, Mail, and Password. Below the Password field, there is a list of requirements: "At least 8 characters", "At least 1 uppercase letter", "At least 1 lowercase letter", and "At least 1 number". A checkbox labeled "I agree to the Terms of Service and Privacy Policy." is present, followed by an orange "Join" button with a checkmark icon.

8.2.2 Creator Sign-In Page

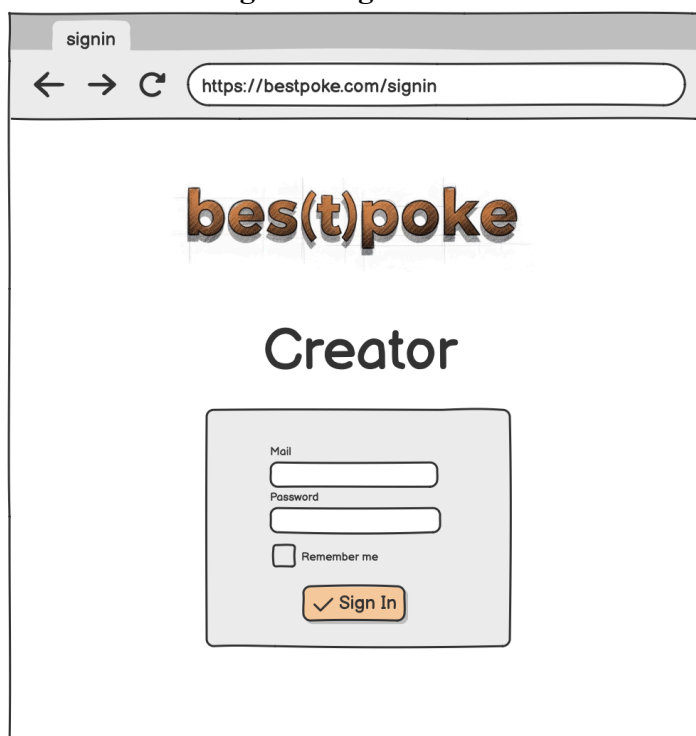


The screenshot shows a web browser window with the address bar displaying "https://bestpoke.com/signin". The page features the "bes(t)poke" logo and the title "Creator". The sign-in form includes fields for Mail and Password. Below the Password field, there is a checkbox labeled "Remember me". An orange "Sign In" button with a checkmark icon is at the bottom of the form.

8.2.3 Creator Home Page

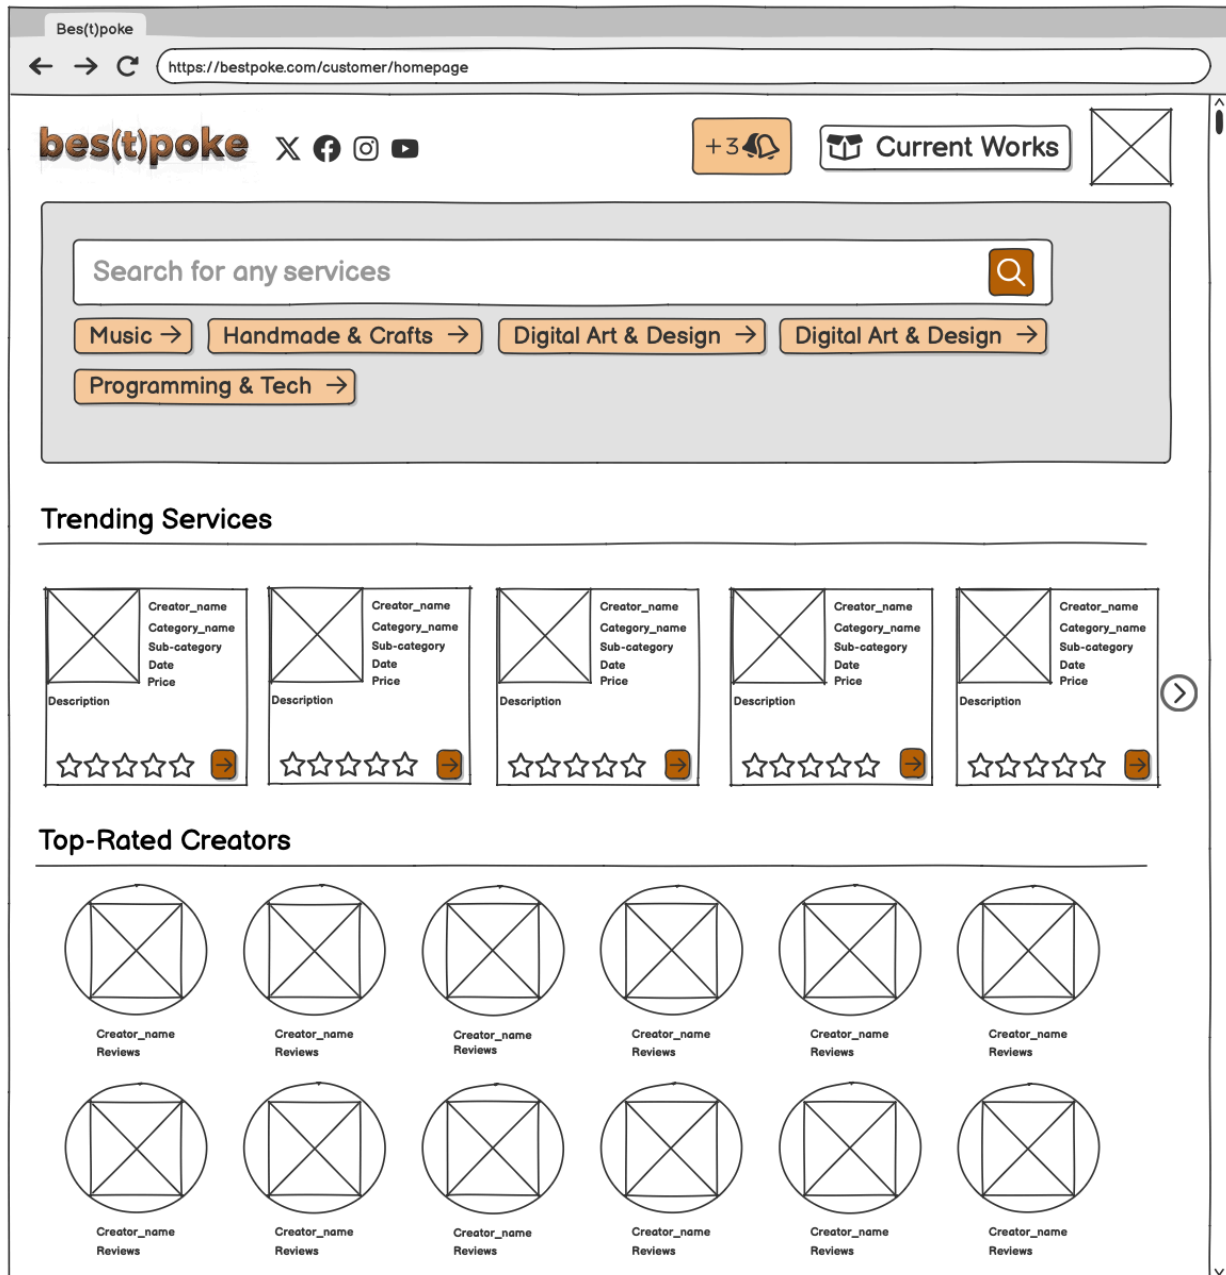

8.2.4 Creator Home Page With Dropdown Menu

Clicking the profile image on the homepage displays the profile dropdown menu.

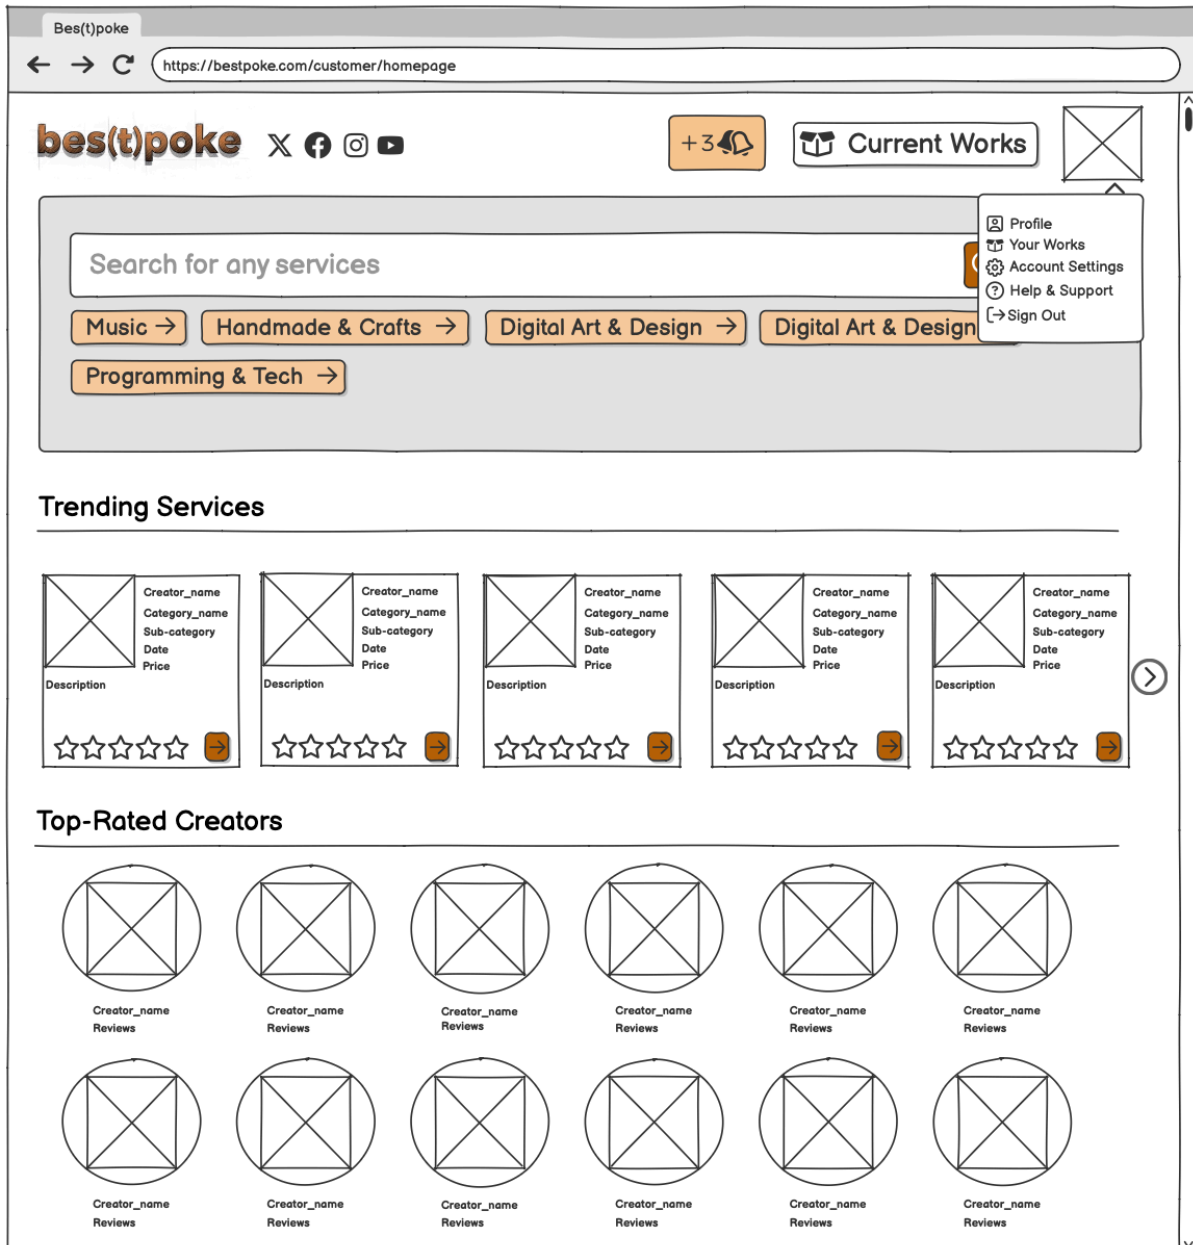

8.2.5 Creator Profile

This page serves as the personal profile dashboard for the creator, allowing them to manage their biography, showcase their certificates, and update their areas of expertise. Through the specialized navigation menu on the left, creators can access the 'Edit Form' section to directly create and build the commission forms from scratch for customers to fill out, and use the 'Your Works' section to view their own previous projects. Additionally, the notification bell icon at the top right allows creators to view incoming alerts from customers and opens the chatbox, enabling them to communicate directly with their clients.

The screenshot shows a web browser window with the URL `https://bestpoke.com/creator/profile`. The page features the **bes(t)poke** logo and social media icons (Twitter, Facebook, Instagram, YouTube) at the top. A notification bell icon with a '+3' badge is in the top right corner. On the left, a navigation menu includes links for 'Edit Form', 'Edit Profile', 'Account Settings', 'Your Works', 'Help & Support', and 'Sign Out'. Below the menu is a placeholder for a profile picture and a '4.2-star rating' with an 'AI Shield Active' badge. The main content area is divided into three sections: 'Biography' with a large text input field, 'Expertise' with buttons for 'SongWriter', 'Pop', 'Music Composition', and 'Ambient', and 'Certificates' with three placeholder boxes. The 'Creator Information' section on the left contains fields for 'Name & Surname' (labeled `Creator_name&surname`), 'Mail' (labeled `Creator_mail`), and 'Address' (labeled `Creator_addres`). At the bottom, there is a 'Social Media' section with icons for Instagram and LinkedIn.

8.2.6 Creator Form Editor Page

This interface allows creators to directly build and structure their custom commission forms from scratch by selecting various functional elements. Additionally, creators can define a maximum revision limit for their services before finalizing and saving the custom order form.

The screenshot displays the 'bes(t)poke' Custom Order Form Builder interface. On the left, a sidebar contains the 'bes(t)poke' logo and a navigation menu with links to 'Dashboard', 'My Portfolio', 'Order Form Builder' (the active page), and 'Account Settings'. A back arrow is located at the bottom left of the sidebar. The main content area is titled 'Custom Order Form Builder' and is divided into two primary sections. The 'Drag & Drop Elements' section on the left lists five form components: 'Text Input', 'Multiple Choice', 'Checkbox', 'Dropdown List', and 'File Upload (Max --)'. The 'Form Preview' section on the right shows a preview of the form with two dummy fields, 'Dummy Field 1' and 'Dummy Field 2'. Below the preview, there is a 'Set Maximum Revision Limit:' label followed by a numeric input field set to '1', with minus and plus buttons for adjustment. A blue 'Save Order Form' button is positioned at the bottom of the preview section.

bes(t)poke

Dashboard
My Portfolio
Order Form Builder
Account Settings

←

Custom Order Form Builder

Drag & Drop Elements
Text Input
Multiple Choice
Checkbox
Dropdown List
File Upload (Max --)

Form Preview
Dummy Field 1
Dummy Field 2
Set Maximum Revision Limit: - 1 +
Save Order Form


8.2.7 Creator Previous Works Page

Bes(t)poke/creator/works

[←](#) [→](#) [↻](#) <https://bestpoke.com/creator/works>

bes(t)poke [X](#) [f](#) [i](#) [v](#)

Creator_name's WORKS




Creator_name

Expertises: #-----, #-----, #-----

Rating: ☆ ☆ ☆ ☆ ☆ --/5

Reviews: --

Product Details



Description:


Tags

Date:

Completion Time:

Price:

Product Details



Description:


Tags

Date:

Completion Time:

Price:

Product Details



Description:

Tags

Date:

Completion Time:

Price:

8.2.8 Creator Edit Profile Page

This interface allows creators to update their professional profile details, including their biography, skills, and contact information. Additionally, they can link their social media accounts and upload certificates before saving the changes via the 'Update' button.



Biography

Skills

Phone:

Addres:

Social Media

Certificate

8.2.9 Account Settings Page

On this screen, users can update their core account configurations, including security credentials, email/SMS notification preferences, and saved credit cards.

The screenshot shows the 'Account Settings' page of the bes(t)poke app. At the top left is the 'bes(t)poke' logo, and at the top right is a close button (X). The page is divided into two main sections: 'Account Settings' and 'Payment Methods'. Under 'Account Settings', there are four text input fields for 'Name', 'Surname', 'Address', and 'Mail'. Below these is a 'Change Password' section with three text input fields for 'Current Password', 'New Password', and 'Confirm Password'. Under 'Preferences', there are two checkboxes: 'Receive Email Notification' and 'Receive SMS Alert'. Under 'Payment Methods', there are two buttons: 'Add Social Media' and 'Manage Saved Cards'. At the bottom of the page is a large blue button labeled 'Save Changes'.

8.2.10 Help and Support Page

This page provides solutions through a Frequently Asked Questions (FAQ) section and allows users to report platform issues or payment disputes by opening a support ticket.

The screenshot shows the 'Help & Support' page of the bes(t)poke app. At the top left is the 'bes(t)poke' logo. The page is divided into two main sections: 'Frequently Asked Questions' and 'Help & Support'. Under 'Frequently Asked Questions', there are four text input fields for 'How does Escrow payment work?', 'How do I request a revision?', 'What is the Dispute process?', and 'Contact Support / Open Ticket'. Under 'Help & Support', there is a dropdown menu labeled 'Select Issue Type' with a downward arrow. Below this is a large text input field labeled 'Describe your problem in detail'. Below that is a text input field labeled 'Upload evidence (optional)'. At the bottom of the page is a large blue button labeled 'Submit Ticket'. A back arrow is located at the bottom left of the page.

8.2.11 Creator Chat Box Page

This interface represents the creator's chatbox, which is used to communicate directly with customers. When an initial commission form is received, the creator evaluates the request and the tentative price to either 'Accept' or 'Decline' the order; once accepted, the system shifts to the 'Drafting' status to track the current stage of the project. Note: Creators cannot initiate contact or send messages to customers first. Interaction is only enabled once a customer fills out the request form and officially initiates the communication.

 	 Customer_name online Price: \$ --
 Customer_name	 Accept Decline
 Customer_name	
 Customer_name	

 	 Customer_name online Price: \$ --
 Customer_name	 Status: Drafting
 Customer_name	
 Customer_name	

8.2.12 Creator Current Works

This page serves as the dashboard where creators can view and track all of their active projects in a centralized table. It allows creators to access project details, customer information, and filled application forms, while enabling them to update the current production status of each order. Once the status is updated, the system automatically triggers a real-time notification that is sent directly to the respective customer's chatbox.



Current Works

Update & Send Notifications

Project Title	Customer Name	Start/End Days	Price	Status	Contact with	Form
project_name	customer_name	start: dd/mm/yyyy deadline: dd/mm/yyyy	--	In production		
project_name	customer_name	start: dd/mm/yyyy deadline: dd/mm/yyyy	--	In production		
project_name	customer_name	start: dd/mm/yyyy deadline: dd/mm/yyyy	--	In production		
project_name	customer_name	start: dd/mm/yyyy deadline: dd/mm/yyyy	--	Drafting		

8.3 Admin's Interfaces

8.3.1 Admin Log in Page

Admin Panel

Authorized personnel only

Email

Password

Two-Factor Authentication Code


Login

Forgot your credentials? Contact system administrator.

 Secured Connection

8.3.2 Admin Dashboard

This interface represents the main Admin Dashboard, providing system administrators with a high-level overview of platform metrics such as total users, active orders, open disputes, and frozen escrow funds. It features a 'Recent Activity' log to track recent user actions and a 'Weekly Order Counts' bar chart to analyze platform performance over the week.

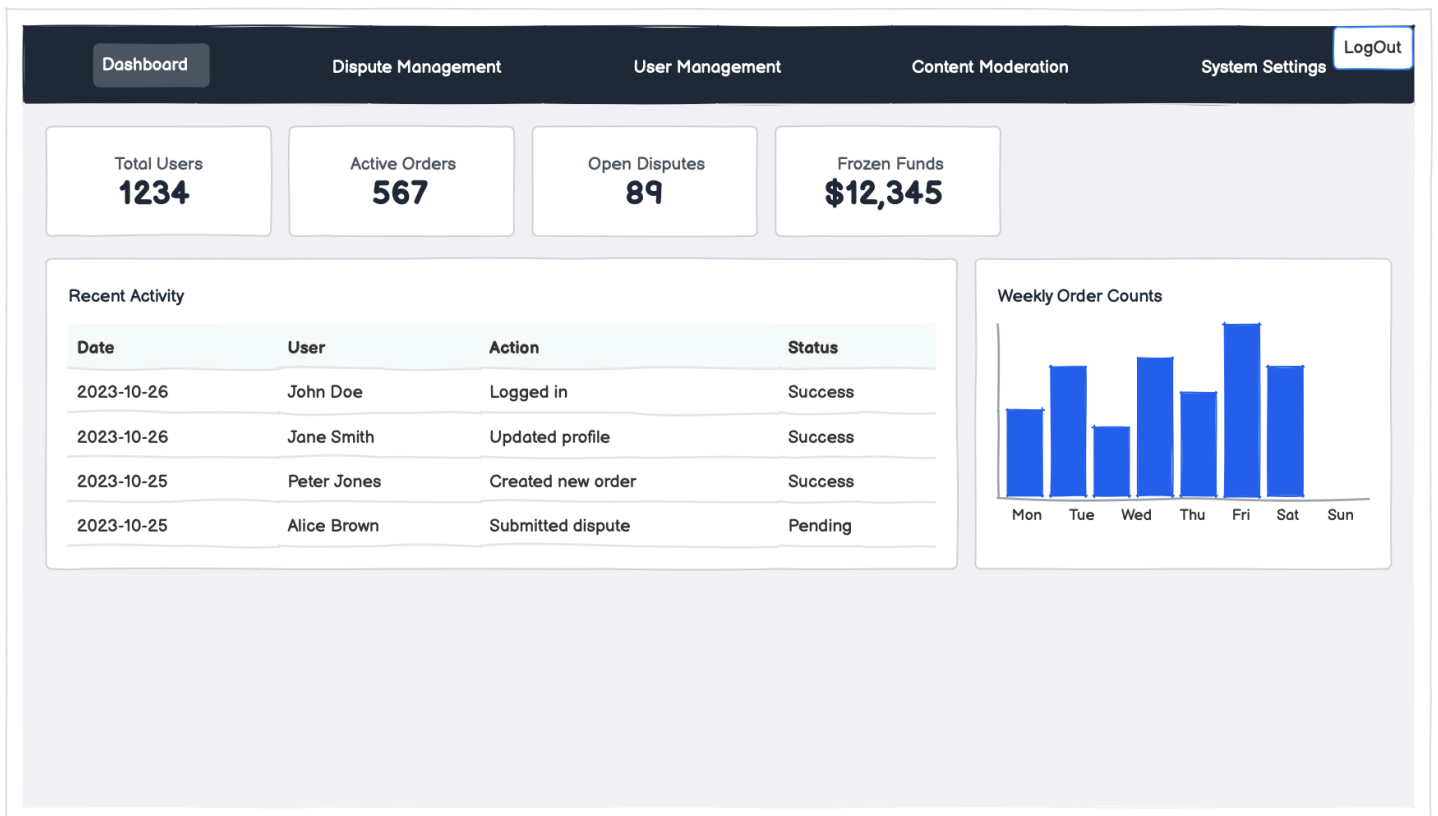

8.3.3 Dispute Management

This interface represents the Dispute Management page, allowing administrators to review and resolve conflicts between buyers and sellers by evaluating submitted statements and evidence. Through this screen, the admin can manage transaction funds using 'Freeze/Unfreeze' actions and finalize the case by ruling in favor of either party, or by issuing a 'Partial Refund'.

DashboardDispute ManagementUser ManagementContent ModerationSystem SettingsLogout

Search Dispute

Dispute ID	Buyer	Seller	Amount	Status	Date	Actions
D1001	Buyer A	Seller X	\$150.00	Pending	2023-10-20	<button>View Details</button> <button>Resolve</button> <button>Freeze Fund</button>
D1002	Buyer B	Seller Y	\$200.00	Open	2023-10-21	<button>View Details</button> <button>Resolve</button> <button>Freeze Fund</button>
D1003	FreezedBuyer C	Seller Z	\$50.00	Resolved	2023-10-18	<button>View Details</button> <button>Resolve</button> <button>Unfreeze Fund</button>

Dispute Details

Buyer Evidence

Buyer's statement...

Seller Evidence

Seller's statement...

Rule for BuyerRule for SellerPartial Refund

8.3.4 User Management

This interface represents the User Management page, enabling administrators to monitor and manage all registered accounts, including customers and creators, in a centralized table. Admins can look up specific profiles using the search and filter functions, view account roles and statuses, and execute moderation controls such as 'Suspend' or 'Ban' to maintain platform safety.

Dashboard

Dispute Management

User Management

Content Moderation

System Settings

LogOut


Search users...

All

User ID	Name	Email	Role	Status	Join Date	Actions
U001	John Doe	john.doe@example.com	Customer	Active	2022-01-15	Suspend Ban
U002	Jane Smith	jane.smith@example.com	Creator	Suspended	2021-11-01	Suspend Ban
U003	Peter Jones	peter.jones@example.com	Customer	Banned	2023-03-20	Suspend Ban
U004	Alice Brown	alice.brown@example.com	Creator	Active	2022-07-10	Suspend Ban

8.3.5 Content Moderation

This interface represents the Content Moderation page, designed for administrators to inspect uploaded images and products to verify if they violate community guidelines. It enables admins to evaluate specific violation reasons—such as nudity, hate speech, or copyright infringement—and execute penal actions by eliminating non-compliant items from the platform using the 'Remove' button.

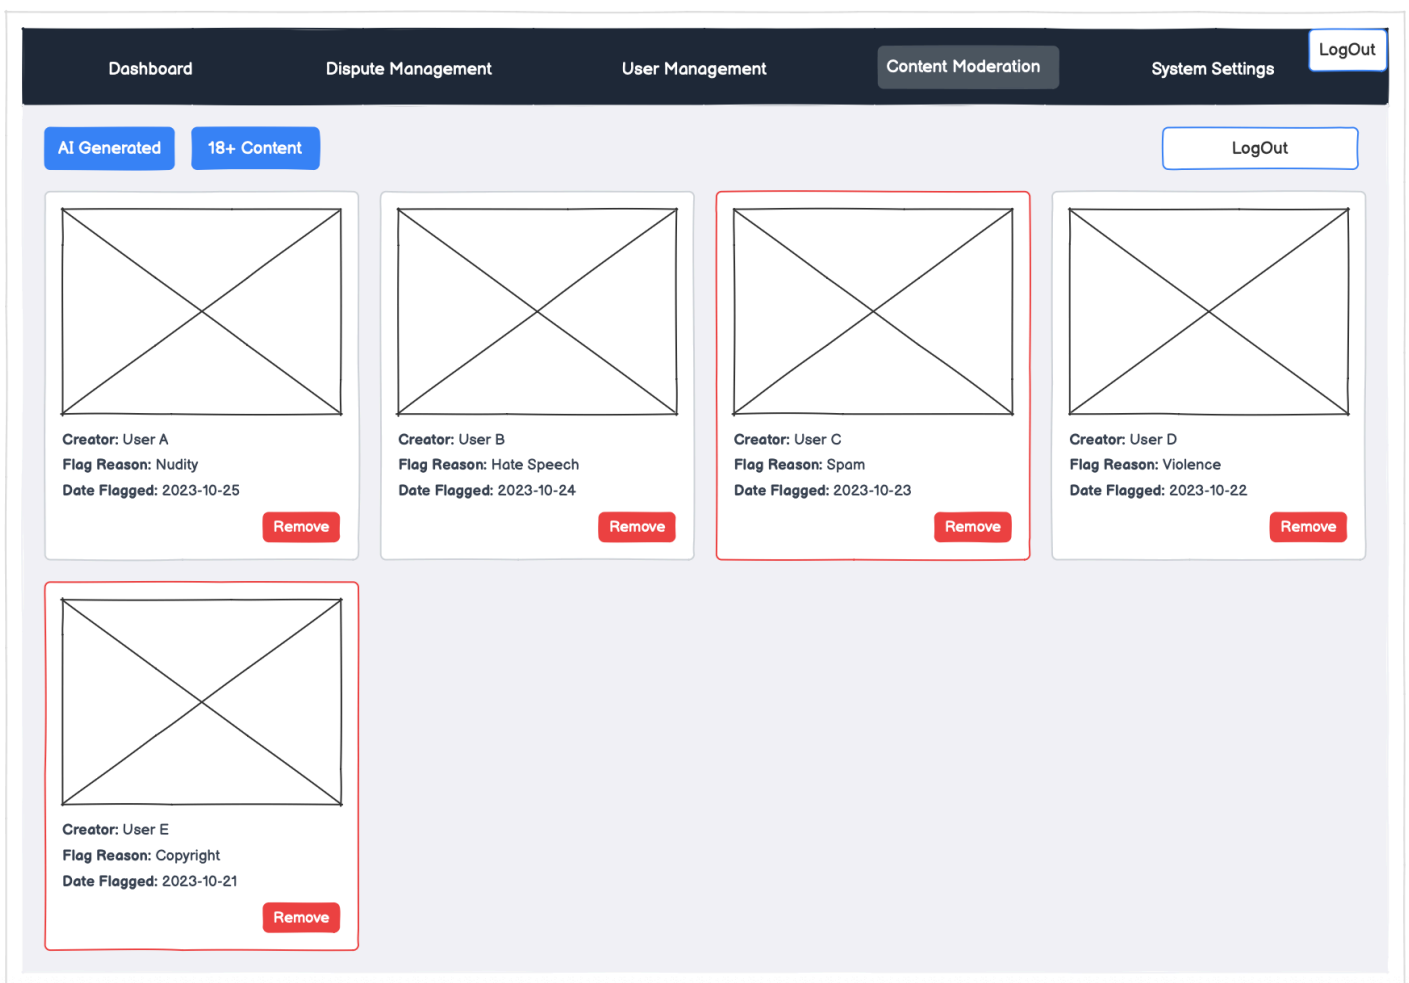

8.3.6 System Settings

This interface represents the System Settings page, which allows administrators to manage core platform configurations. Admins can schedule system maintenance with custom dates and messages, instantly enable or disable new user registrations via the 'Registration Control' toggle, and publish platform-wide announcements to all users.

DashboardDispute ManagementUser ManagementContent ModerationSystem SettingsLog Out

Maintenance Mode

Maintenance Start

mm/dd/yyyy

hh:mm

Maintenance End

mm/dd/yyyy

hh:mm

Maintenance Message

Enter message to display during maintenance...

Schedule Maintenance

Cancel Scheduled Maintenance

Registration Control

New user registrations can be enabled or disabled instantly.

Allow New Registrations

Platform Announcement

Announcement Message

Enter your announcement here...

Send Announcement

9.0 Conclusion

In conclusion, this Software Development Plan (SDP) details the engineering and project management steps required for the Bes(t)poke project to achieve its core objectives.

To manage the uncertainties and risks in the freelance ecosystem, our eight-person team has adopted the flexible Agile Scrum methodology and planned the development process across four main Sprints.

To ensure the reliability and scalability of the system, AWS cloud infrastructure, React.js for dynamic user interfaces, and .NET Core combined with MS SQL Server for financial transactions requiring high data integrity were strategically selected.

Furthermore, potential project risks have been thoroughly analyzed, and non-functional requirements such as performance and legal security (Compliance) have been tied to strict criteria.

Through all this meticulous planning and robust technological infrastructure, the Bes(t)poke team is fully prepared to launch this platform, which prevents fraud, eliminates time-wasting, and provides a fair earning environment for digital creators.
